


MOBILE & MANUFACTURED HOMES CHECKLIST

Date: _____
Permit Number: _____
Applicant/Owner: _____
Rural or Street Address: _____
Legal Land Description: Lot _____ Block _____ Plan _____
 _____ ¼ Sec _____ Twp _____ Rge _____ W of _____ M

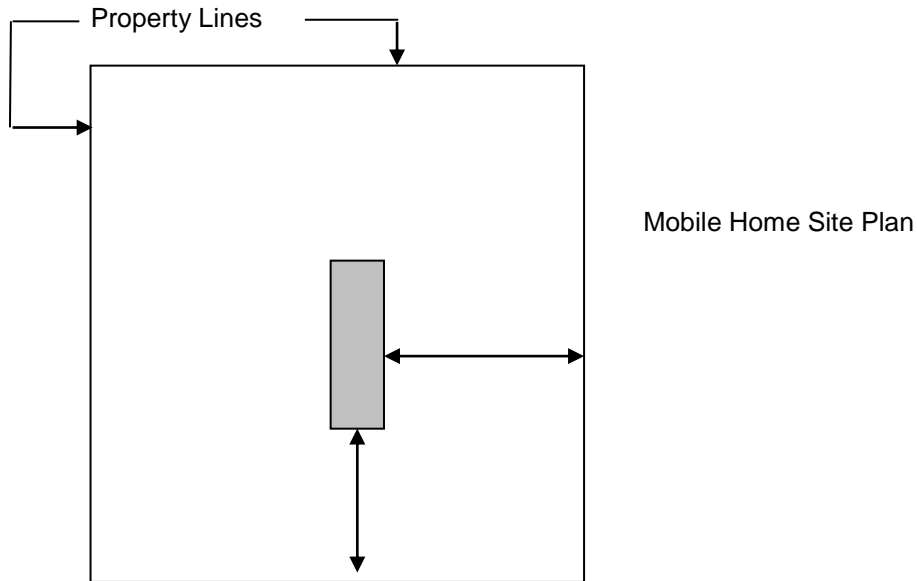

CERTIFICATION LABELS:

CSA Label #: _____
AMA Label #: _____
Year of Manufacture: _____
Model / Serial #: _____

Please check off boxes that apply to your mobile home set up and attached this form to your building permit application.

FOUNDATION:

- Concrete Piling as per CSA
 - Wood Blocking as per CSA
 - Concrete Blocking
 - Engineered Screw Piling
(Must be fabricated by CWB certified welder)
 - Building anchorage to be provided where required.
 - Foundation as per Part 4 or 9 of the ABC 1997
 - Refer: CSA-Z240.10.1.94
- Others: _____

DECKS/STAIR LANDINGS

- Stairs: Rise: 125mm to 200mm (5" to 8")
Run: 210mm to 355mm (8-1/4" to 14")
Tread: 235mm to 355mm (9-1/4" to 14") Others: _____
- Handrail: 800mm to 965mm ht. (32" to 38")
required for exterior stairs with >3 risers. Others: _____
- Guards: 900mm ht. (36") required for decks/landings
600-1800mm ht. (2' to 6') above the adjacent grade.
1070mm ht, (42") for decks/landing >1800mm above grade.

CRAWLSPACE:

- Clearance: 24" between grade & bot. of floor joists Others: _____
- Ventilation min. 1ft²/50ft² of crawl space area
- Access hatch 500mm x 700mm (20"x28") min.
- Ground shall be graded min 2% for proper drainage.
- Ground cover 0.1mm poly Others: _____
